



Matilija Road Emergency Project at MP 2.25

Board of Supervisors Presentation

October 29, 2024

Presented by: Anitha Balan, Director of Roads & Transportation


Agenda

- Matilija Road Storm Damage Emergency Repairs at MP 2.25
- Emergency Declaration & Contracting Process
- Cost and Schedule of Emergency Repairs
- Status of Current Project
- Recommended Board Action

Matilija Road Emergency work at MP 2.25



Before Damage, Summer 2023

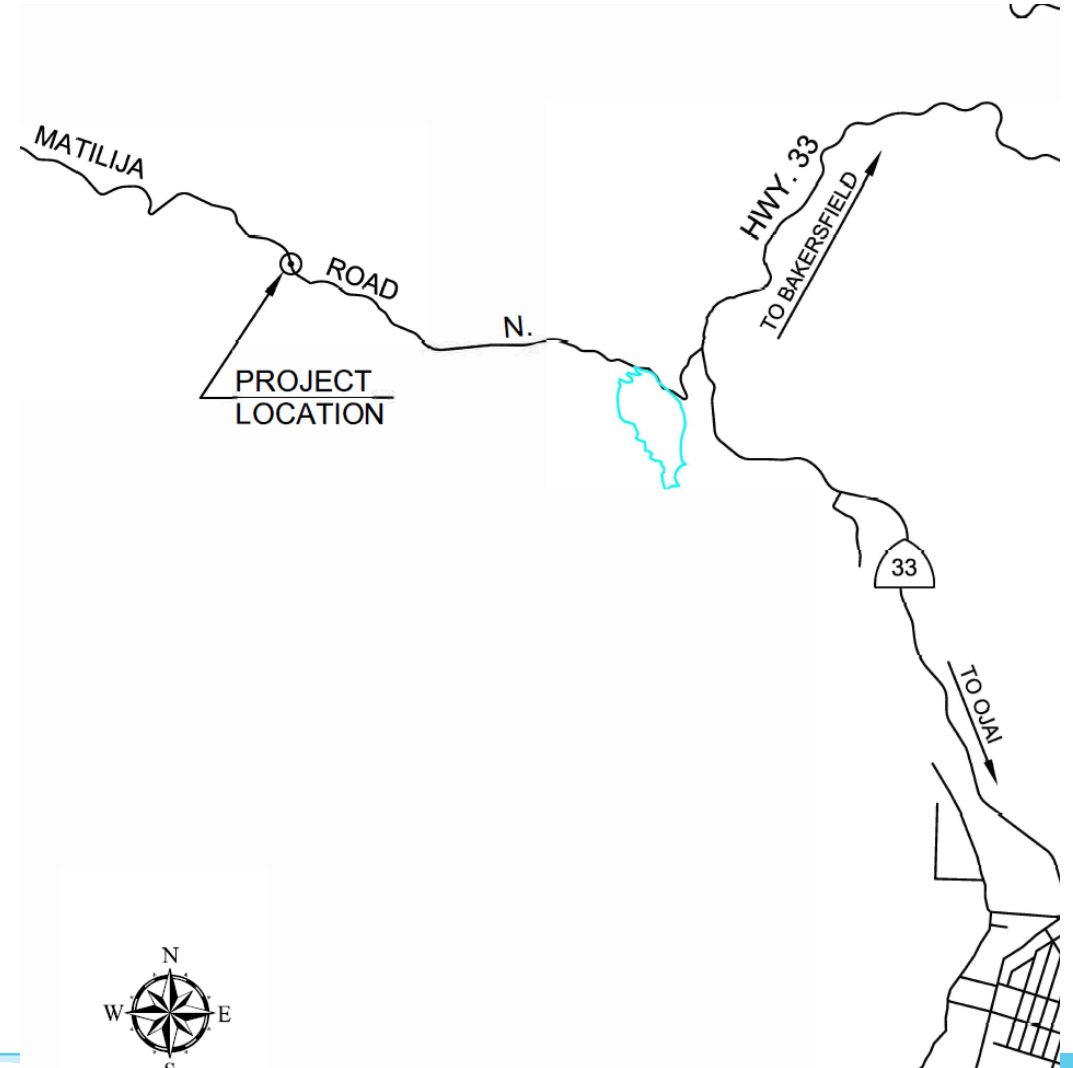

Damage & Concerns Identified

- Damage reoccurred February 2024 Storms; Road Closed & one lane access maintained for small vehicle
- In September Fire Dept & Cal OES identified urgent need for Emergency Access
 - High Potential for Fire fueled by strong wind
 - Only Emergency Evacuation Access for residents



Actions Taken – Matilija Road MP 2.25

- Director of Public Works Agency Declared Emergency (9/10/24)

- PWA Obtained Regulatory Permits (9/27/24)
 - Emergency Permit (RGP-63 Permit) from Army Corps of Engineers
 - Regional Water Quality Control Board (401 Permit)
 - California Department of Fish & Wildlife (1610 Permit)

- PWA Awarded a Construction Contract through the Emergency Bidding process (9/16/ – 9/23)
 - Solicited bids from 4 local contractors – 2 bids received
 - Awarded Contract with Union Engineering Company, Inc. (Low Bid)

Actions Taken – Matilija Road MP 2.25

- Contracted with 3 Consultants (9/23/24 – 9/25/24)
 - Galvin Preservation Associates, Inc. for Environmental Compliance and Monitoring
 - MNS Engineers, Inc. for Construction Inspection
 - Union Materials, Inc. for Materials Testing
- Secured Right of Entry from property owner (Matilija Canyon Alliance on 9/28/24)
- Public/Resident Notifications
 - Social media
 - Notices/Letters sent to residents
 - Construction Notices on site/CMS Board

Project Cost – Matilija Road MP 2.25

- Estimated Projected Cost: **\$ 2,172,540.00** (Including all costs)
 - Construction Contract
 - Award to Union Engineering Company Inc. of Ventura for **\$1,679,238.00**
 - Design & other Costs
 - Design & contract prep (In-House)
 - Construction Inspection provided by MNS Engineers. \$74K
 - Materials Testing by Union Materials Testing, Inc. \$60K
 - Environmental Support by Galvin Preservation Associates, inc. \$152K
- PWA is seeking FEMA reimbursement
 - Reimbursement at 75%
 - Not guaranteed

Project Schedule – Matilija Road MP 2.25

- Notice to proceed issued September 27,2024
 - 45 Calendar Days to complete the project
 - Contractor is working extended Days & Saturdays
 - Project is on schedule
- Estimated completion date – Mid-November

Current Condition



Recommended Board Actions

- Receive and File a Report on the Status of Work completed for the Matilija Road North Emergency Repairs at MP 2.25
- Determine the Need to Continue the Emergency Action

Questions?
