

CONTRACT CHANGE ORDER NO. 1

With Summer Construction, Inc

Old Telegraph Road Bridge Emergency Repairs – Project No: P6X50659

Spec No. RD24-07(E)

Public Works Agency

Contracting Agency: County of Ventura

CONTRACT CHANGE ORDER NO. 1**Project Name: Old Telegraph Road Bridge #485 Emergency Repairs**

ACCOUNTING	A/C Contract No.	Budget Dept/Acct No.	Project No.
DATA:		4081-2184	P6X50659

To: Summer Construction, Inc.

You are hereby directed to make the following changes to the plans and specifications for this contract.

Note: This change order is not effective until approved by the Board of Supervisors, Director of Public Works Agency, a Department Director (as Deputy Director - Public Works Agency) or Deputy Purchasing Agent, as indicated.

1.1 Add new Contract item, Shotcrete Void Under Wingwall

Prepare cavity under wingwall, install rebar & wire mesh, shotcrete cavity to fill void in Exhibit 1

+1 LS.....\$ 12,804.00

1.2 Add new Contract item, Place Class II Base under riprap Per Exhibit 2

+16 TN @ \$80/TN.....\$ 1,280.00

1.3 Add new Contract item, Place Filter Fabric under riprap Per Exhibit 2

+1 LS.....\$2,700.00

1.4 Increase the Quantity of Contract Item #6, Riprap

+805 ton@\$165.00/TN.....\$ 132,825.00

1.5 Add new Contract item, Riprap toe bench on upstream side of abutment

Replace Sheet 1 of the plans with Sheet 1R per Exhibit 2

668 TN @ \$196.00/TN\$ 130,928.00

1.6 Add new Contract item, Re-mobilize

1 LS @ \$10,000/LS\$ 10,000.00

The total cost of this Contract Change Order is \$290,537.00

By reason of this order, the time of completion will be adjusted as follows:	Contract Time is extended by 15 Calendar Days
--	---

RECOMMENDED *Perry Hoon* REG. NO. 62876 DATE 3/21/2024

FOR APPROVAL BY: Director - Public Works Agency

APPROVED BY *[Signature]* DATE 3/22/24

The undersigned contractor has given careful consideration to the change proposed, including its effect on other work already contracted for, and hereby agrees, if this change order is approved, that he will provide all equipment, furnish all materials, except as may otherwise be noted above, and perform all services necessary for the work above specified, and will accept as full payment for all costs related in any way thereto the prices shown above.

ACCEPTED, CONTRACTOR

BY *[Signature]* TITLE President DATE 3/22/2024

Spec No. RD24-07(E)

Public Works Agency

Contracting Agency: County of Ventura

CONTRACT CHANGE ORDER NO. 1

Project Name: Old Telegraph Road Bridge #485 Emergency Repairs

If this contract change order is executed by the Agency, but the Contractor does not sign it, the Contractor shall, as required by the Specifications cited:

1. Proceed with the ordered work (Subsections 3-2.2.3 and 3-5);
2. File a written Notice of Potential Claim before commencing the work ordered (Subsection 6-11); and
3. Keep and furnish daily records of materials, equipment and labor (Subsections 3-3.3 and 3-5)

Original: Contractor. Copies: Auditor, Project Manager, Contracts Div, Client, Inspector, Fiscal, AE, Project File


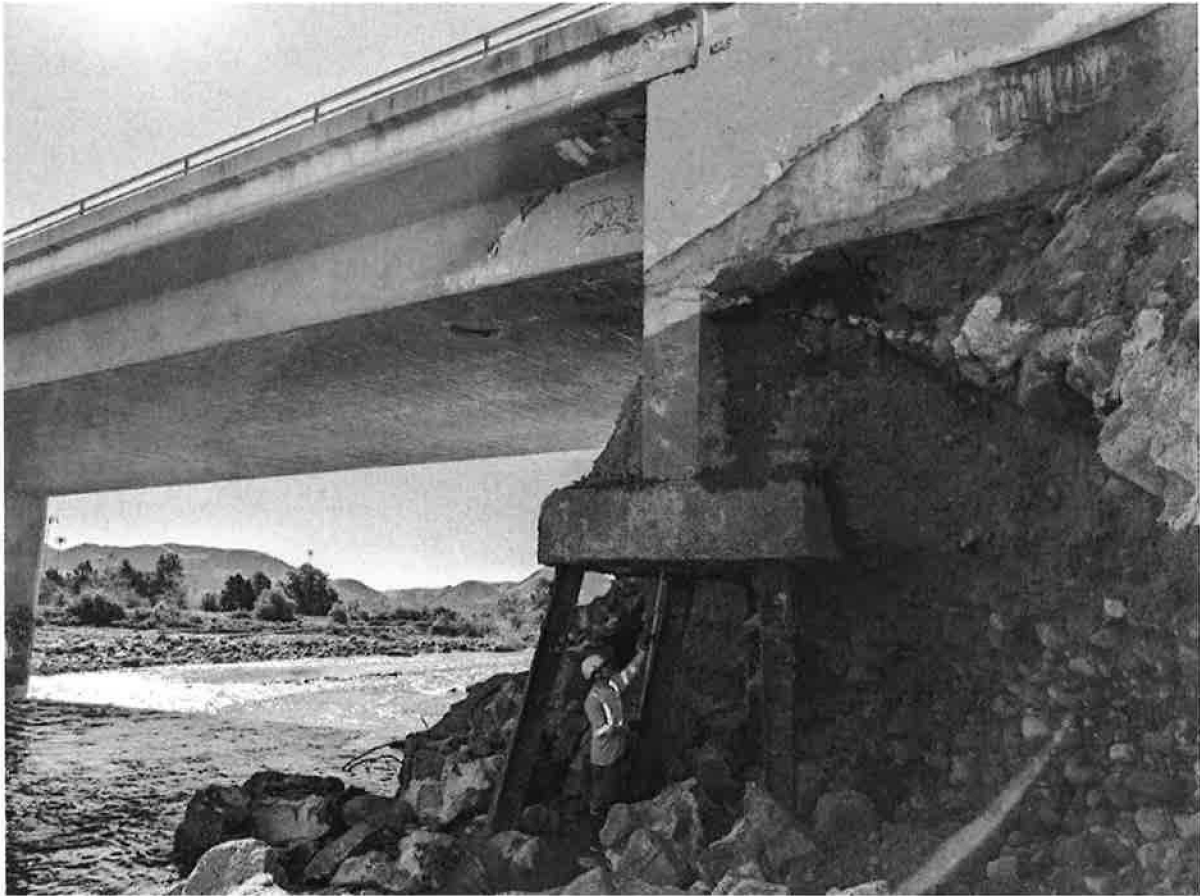



Figure 7: Elevation view of Abutment 1 looking South. Piles are exposed approximately 9-ft.

Exhibit 1

LAYOUT DRAWING

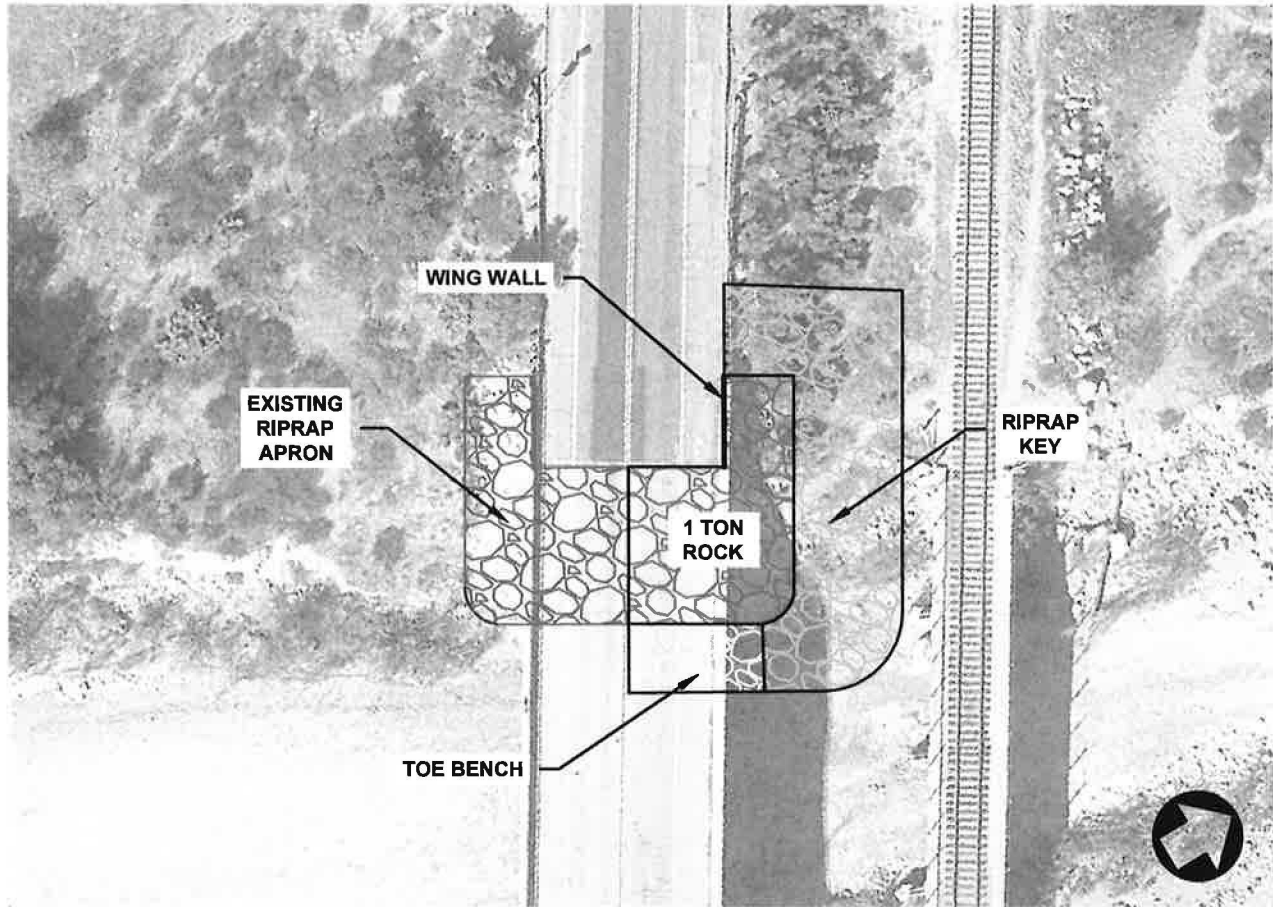


RIPRAP KEY

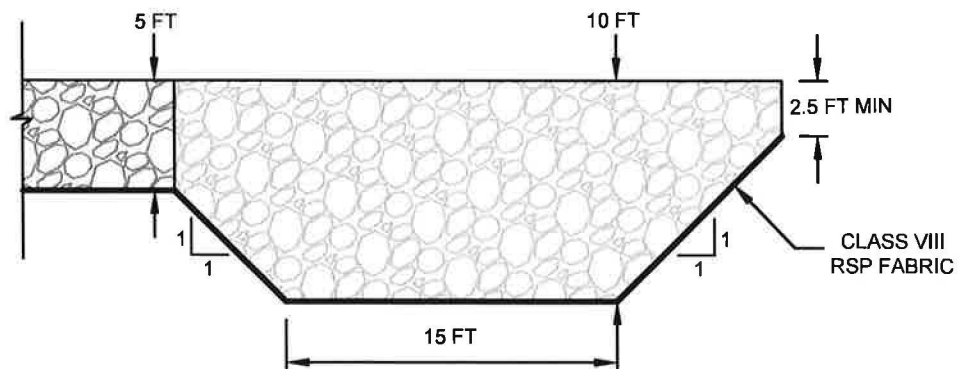

CONSTRUCT KEY ON UPSTREAM SIDE OF CLASS VIII RIPRAP ON APPROACH SLOPE & OVBANK OUTSIDE THE AREA SUPPORTED BY THE "TOE BENCH".

DRAWN _____ EM	COUNTY OF VENTURA PUBLIC WORKS AGENCY ROADS & TRANSPORTATION DEPARTMENT	RD24-07(E) SPEC. NO.
DESIGNED _____ TH		P6X50659 PROJ. NO.
CHECKED _____	OLD TELEGRAPH ROAD BRIDGE #485 EMERGENCY REPAIRS	SHEET 1R
APPROVED _____		

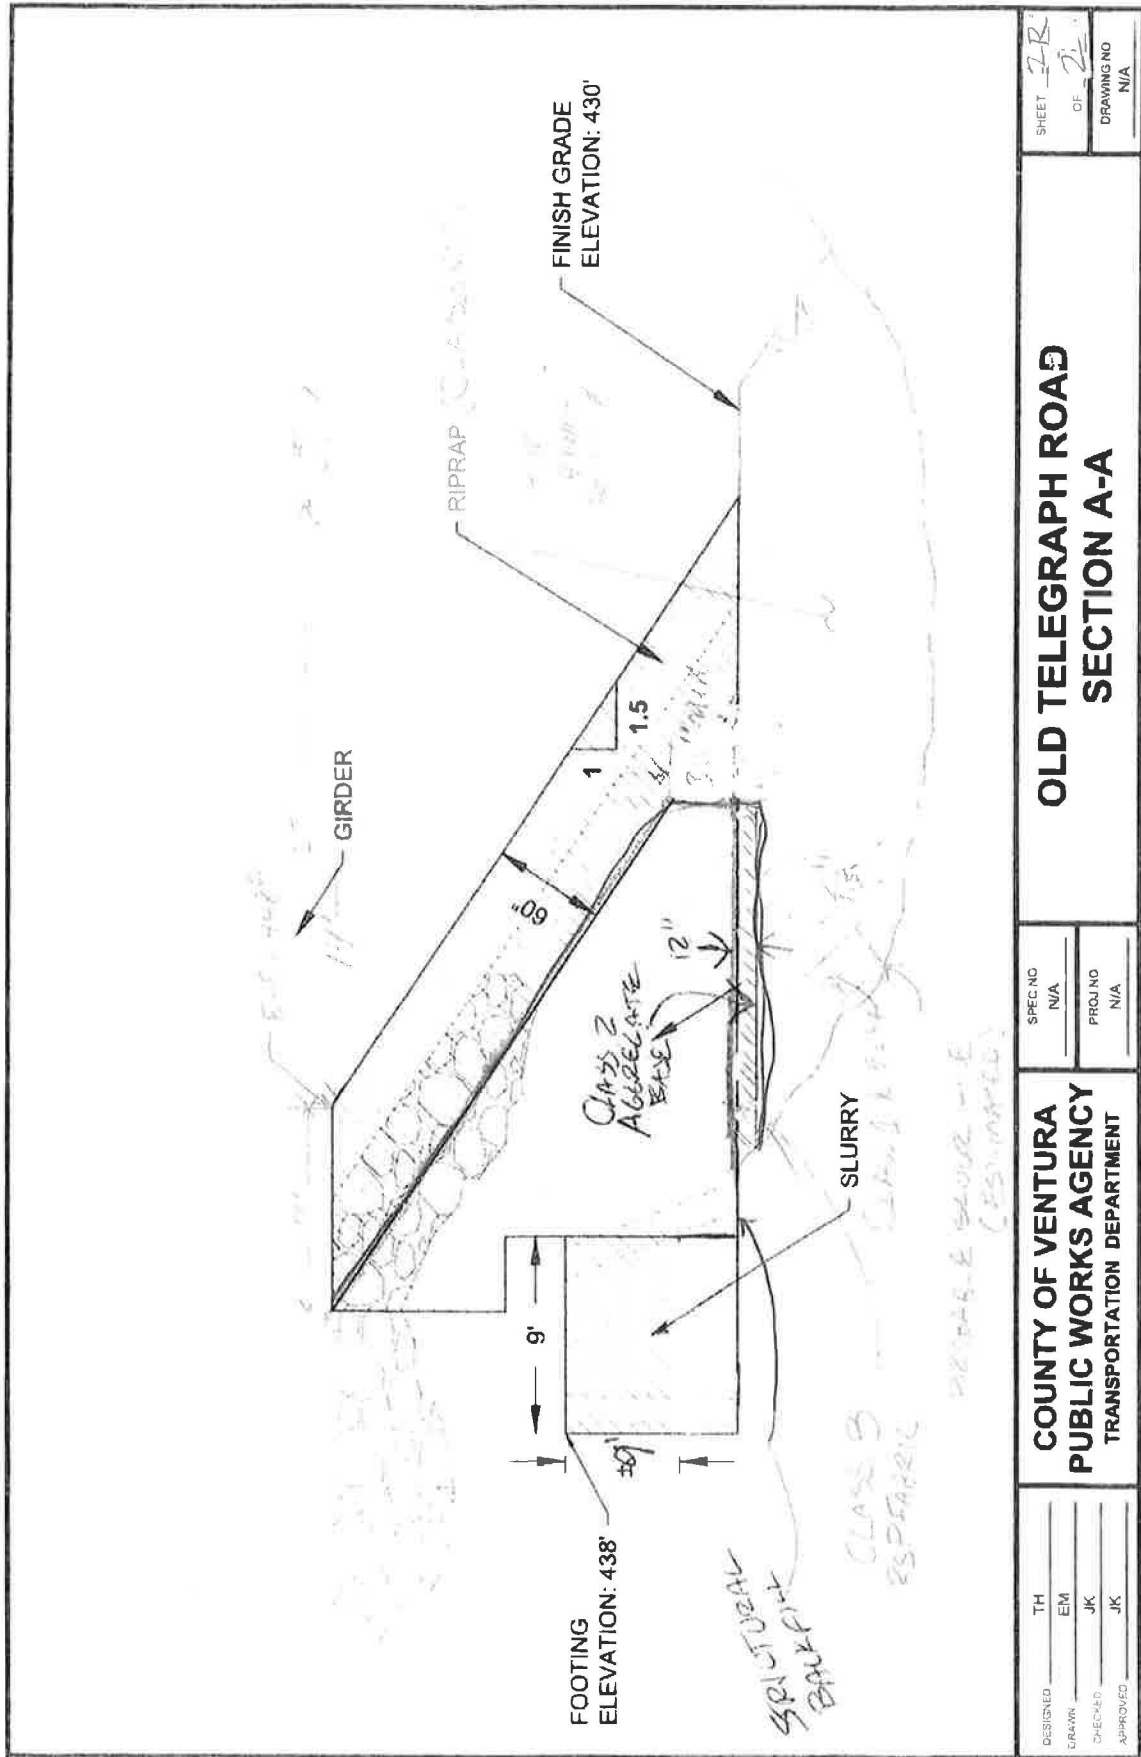

DESIGNED _____ DRAWN _____ CHECKED _____ APPROVED _____		COUNTY OF VENTURA PUBLIC WORKS AGENCY TRANSPORTATION DEPARTMENT		SPEC. NO. N/A	OLD TELEGRAPH ROAD SECTION A-A		SHEET <u>2-B</u> OF <u>2</u> DRAWING NO. N/A
--	--	---	--	------------------	---	--	---
